


LIBRARY LEARNING COMMONS

Plans for Renovation to the Academic Spine, E - Wing

LOGISTICS PLAN

PROJECT LOCATION

Aerial Photograph

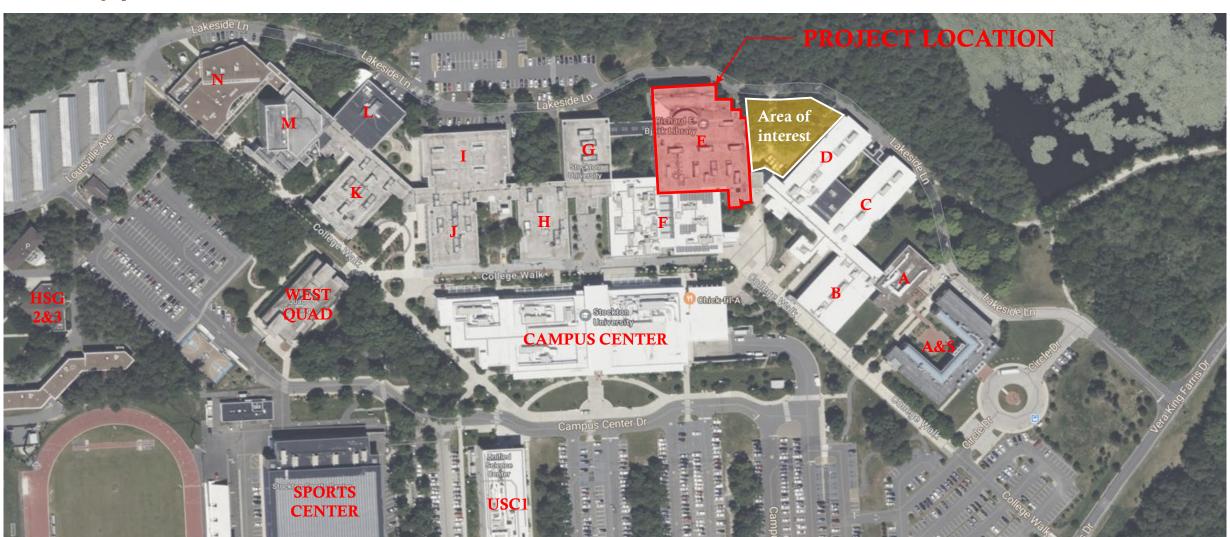






CURRENT SPACE UTILIZATION


Aerial Photograph



Dept Code	Dept Name	Area
ADF	Adminstration and Finance	4,512
ARHU	School of Arts and Humanties	2,477
GRAPH	Graphics	2,264
LIBRY	Library Services	11,485
MEDIA	PRODUCTION SERVICES	4,256
PLANT	Plant Operations	1,403
TELEC	Telecommunications & Network Infrastructure	20
Total		26,417

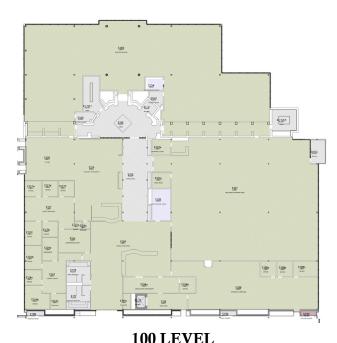

Dept Code	Dept Name	Area
HLTH	Health & Wellness	294
LIBRY	Library Services	24,920
PLANT	Plant Operations	2,892
TELEC	Telecommunications & Network Infrastructure	26
Total		28,132

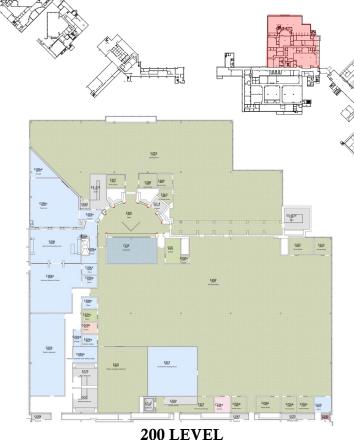


Dept (ie	Area
AAF	Academic	Affairs	473
BUSN	School of	Business	64
GENS	School of	General Studies	5,088
LIBRY	Library Se	ervices	20,112
NAMS	School of	Natural Sciences and Math	201
PLANT	Plant Ope	rations	1,065
SOBL	Social and	d Behavioral Sciences	90
TELEC	Telecomm	unications & Network Infrastr	ructure 15
Total			27,108





RELOCATION PLAN – MULTIPLE MOVES


Academic Spine – 000 Level

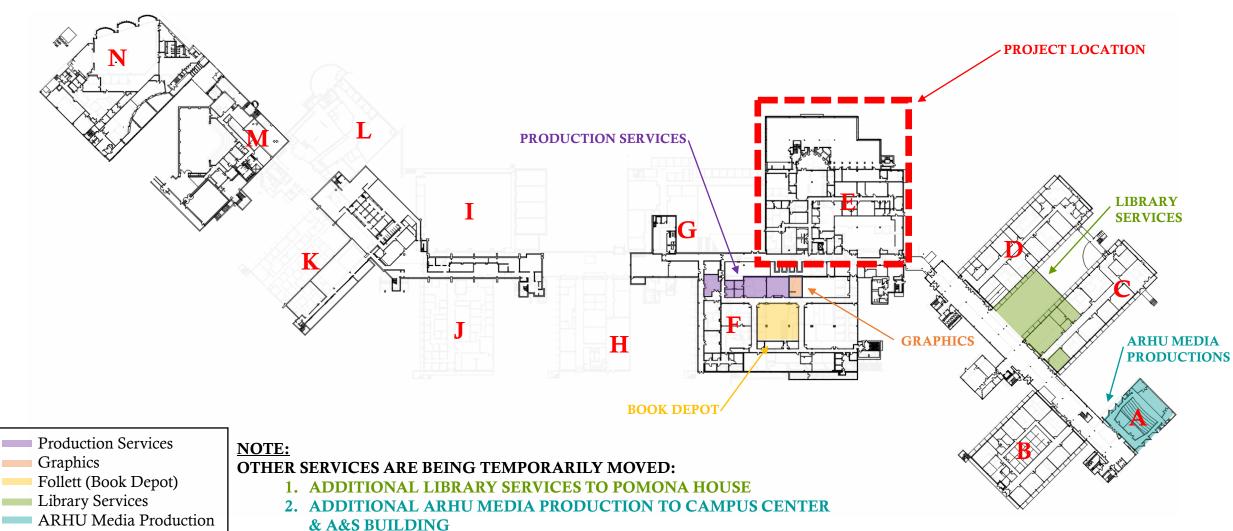



RELOCATION PLAN – MULTIPLE MOVES

Academic Spine – 100 Level

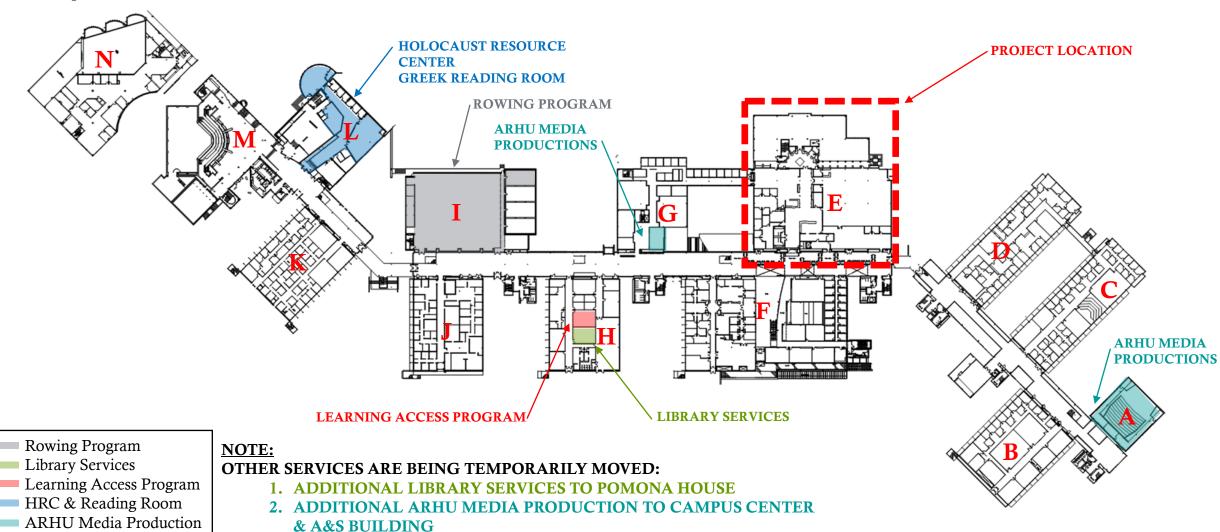







GALLERY COMPUTER STATIONS

Academic Spine - 000 & 100 Level

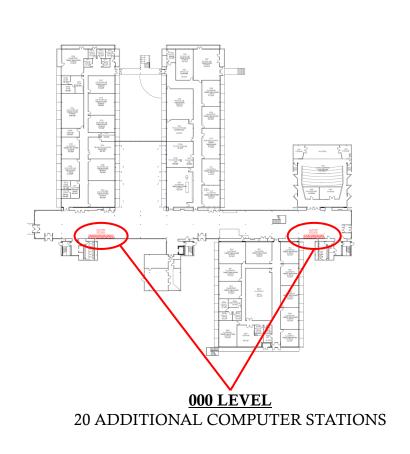


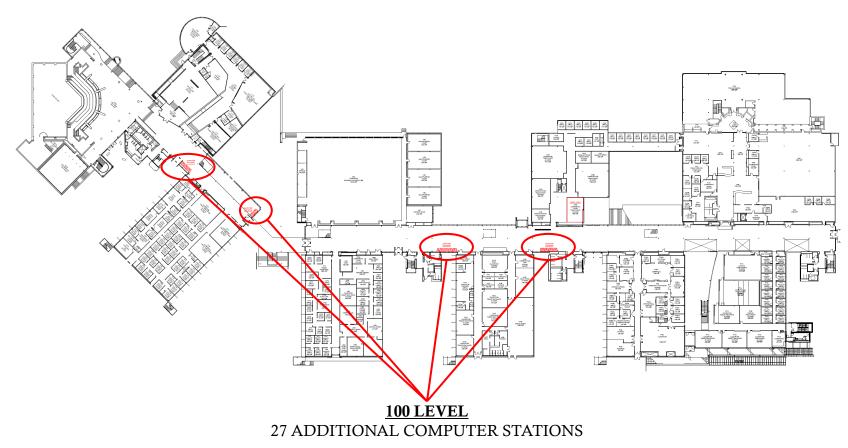




PRODUCTION SERVICES

E-Wing - Lower Level 000

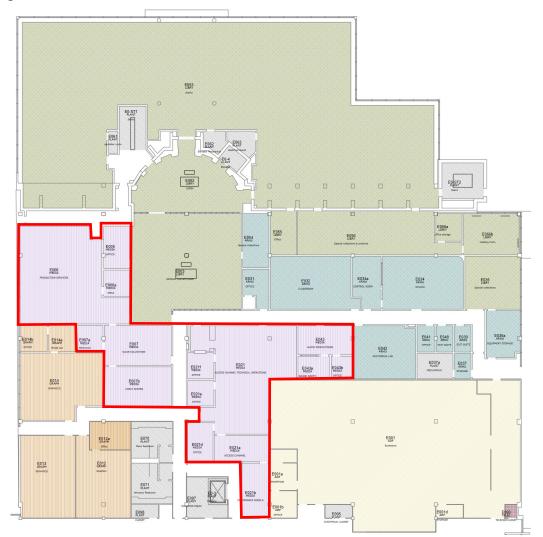




Dept Code	Dept Name	Area
ADF	Adminstration and Finance	4,512
ARHU	School of Arts and Humanties	2,477
GRAPH	Graphics	2,264
LIBRY	Library Services	11,485
MEDIA	PRODUCTION SERVICES	4,256
PLANT	Plant Operations	1,403
TELEC	Telecommunications & Network Infrastructure	20
Total		26,417





PRODUCTION SERVICES

F-Wing - Lower Level 000

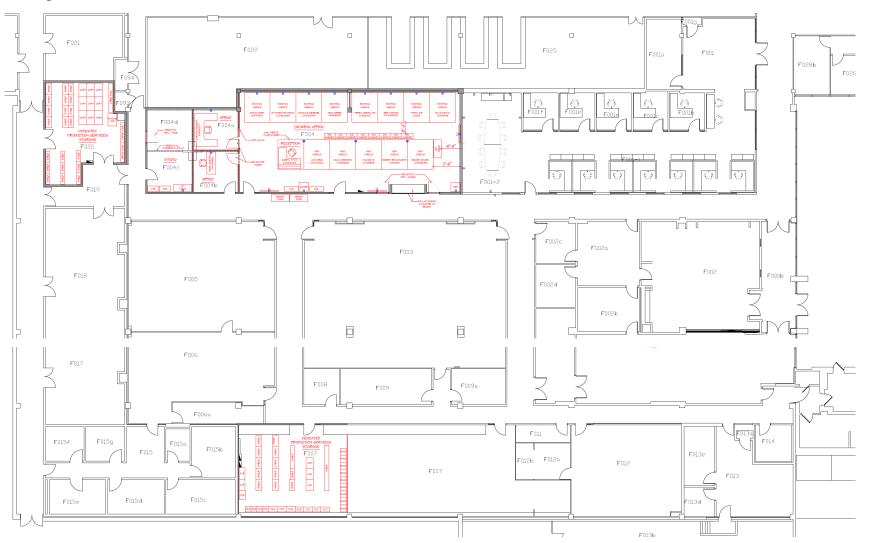



Improvement Status

F004

- Rowing has been relocated to I-Wing.
- · Hauserman walls have been removed.
- Plumbing has been removed and capped.
- Metal wall framing underway.

F020


- NAMS cleared all their items from the space.
- · All casework has been removed.
- Final paint complete.







GRAPHICS

E-Wing - Lower Level 000

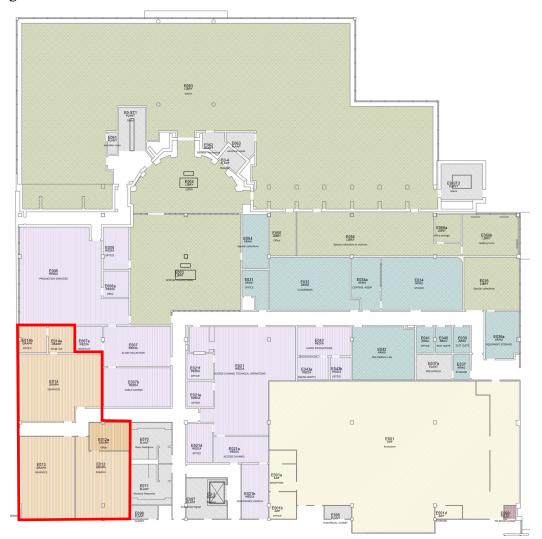





Dept Code	Dept Name	Area
ADF	Adminstration and Finance	4,512
ARHU	School of Arts and Humanties	2,477
GRAPH	Graphics	2,264
LIBRY	Library Services	11,485
MEDIA	PRODUCTION SERVICES	4,256
PLANT	Plant Operations	1,403
TELEC	Telecommunications & Network Infrastructure	20
Total		26,417






GRAPHICS

F-Wing - Lower Level 000

Improvement Status





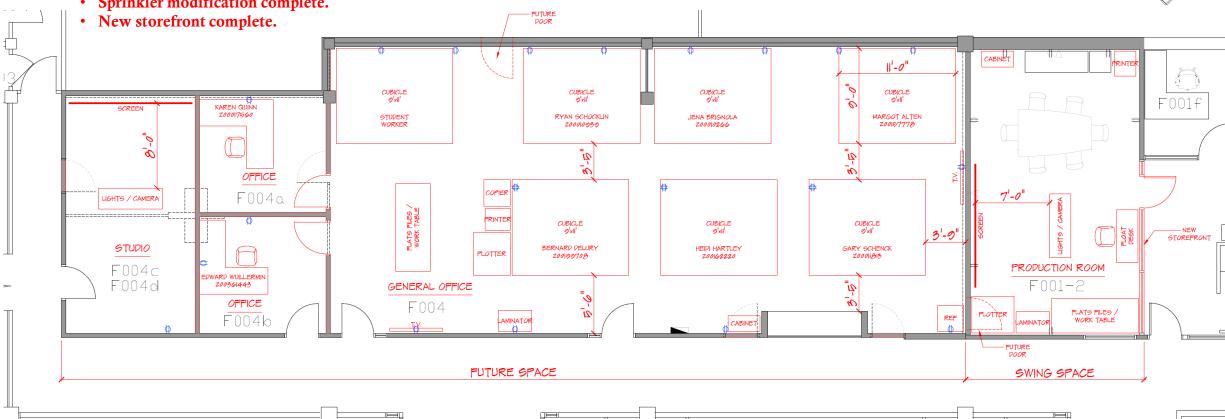







FOLLETT

E-Wing - Lower Level 000

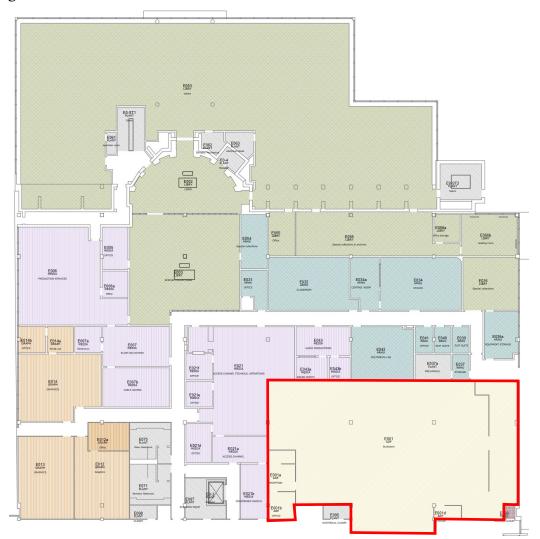



Dept Code	Dept Name	Area
ADF	Adminstration and Finance	4,512
ARHU	School of Arts and Humanties	2,477
GRAPH	Graphics	2,264
LIBRY	Library Services	11,485
MEDIA	PRODUCTION SERVICES	4,256
PLANT	Plant Operations	1,403
TELEC	Telecommunications & Network Infrastructure	20
Total		26,417






FOLLETT

F-Wing - Lower Level 000







Improvement Status

- NAMS cleared all their items from the space.
- · All casework has been removed.
- Trench panels were fabricated and installed.
- Metal wall framing has been completed.
- New ceiling and lighting complete.
- Final paint underway.
- · Carpet installation anticipated next week.
- Followed by books / bookshelf relocation.



E-Wing - Lower Level 000

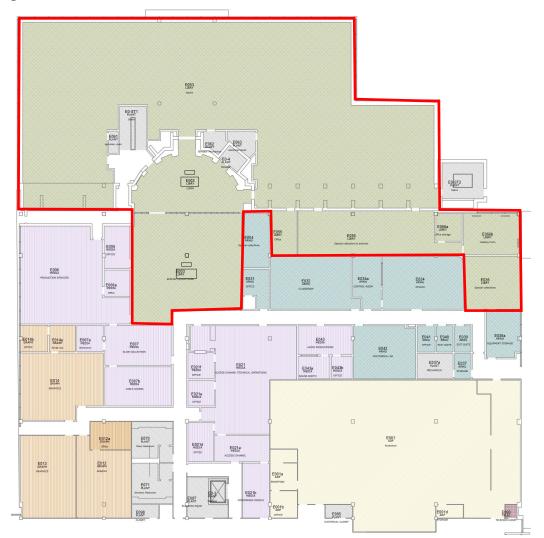





Dept Code	Dept Name	Area
ADF	Adminstration and Finance	4,512
ARHU	School of Arts and Humanties	2,477
GRAPH	Graphics	2,264
LIBRY	Library Services	11,485
MEDIA	PRODUCTION SERVICES	4,256
PLANT	Plant Operations	1,403
TELEC	Telecommunications & Network Infrastructure	20
Total		26,417





E-Wing - Main Level 100

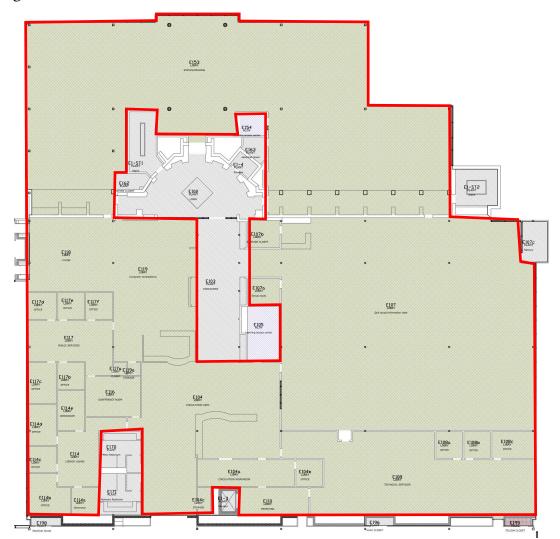





Dept Code	Dept Name	Area
HLTH	Health & Wellness	294
LIBRY	Library Services	24,920
PLANT	Plant Operations	2,892
TELEC	Telecommunications & Network Infrastructure	26
Total		28,132





E-Wing - Upper Level 200

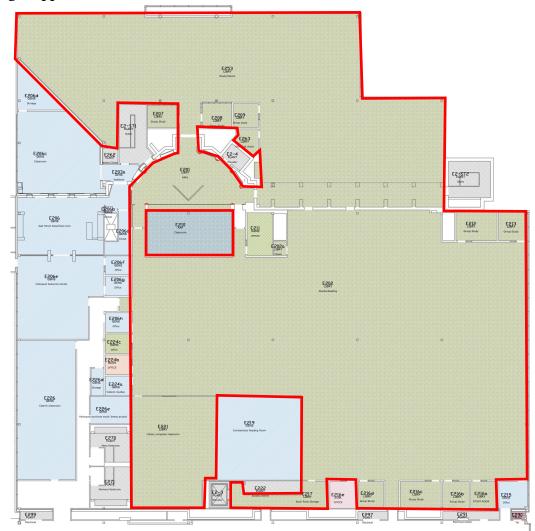





Dept Code	Dept Name	Area
AAF	Academic Affairs	473
BUSN	School of Business	64
GENS	School of General Studies	5,088
LIBRY	Library Services	20,112
NAMS	School of Natural Sciences and Math	201
PLANT	Plant Operations	1,065
SOBL	Social and Behavioral Sciences	90
TELEC	Telecommunications & Network Infrastructure	15
Total		27,108





C/D-Wing - Lower Level 000

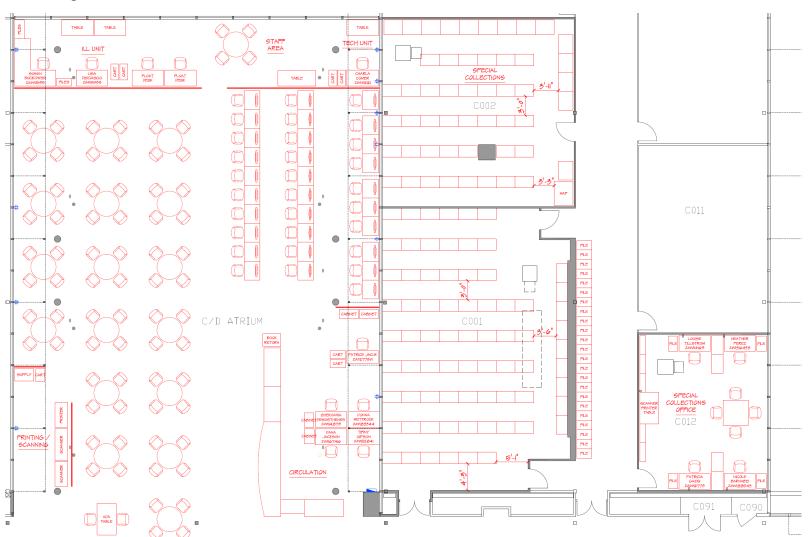




Improvement Status


- C001 demo to immediately follow commencement.
- Book packing scheduled for 05/20 06/07.
- C/D atrium setup will commence sometime in August after ITS's upgrades to the atrium space.







H-Wing - Main Level 100

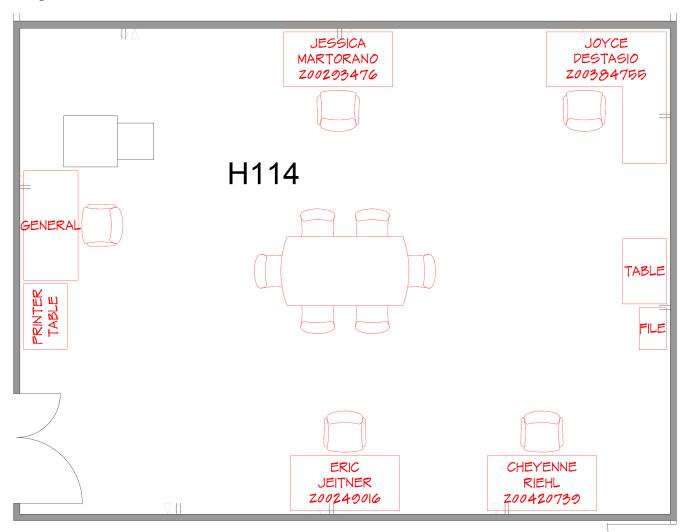



Pomona House - Main Level 100

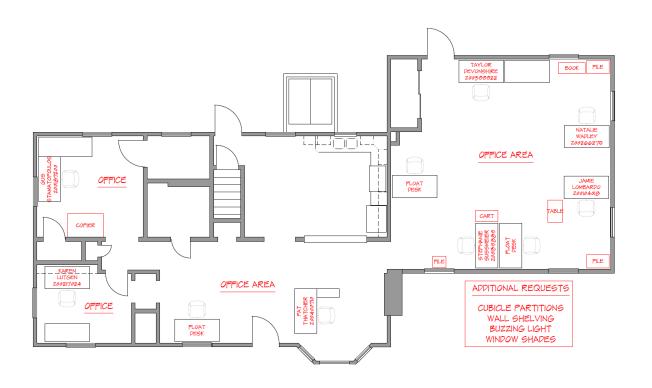

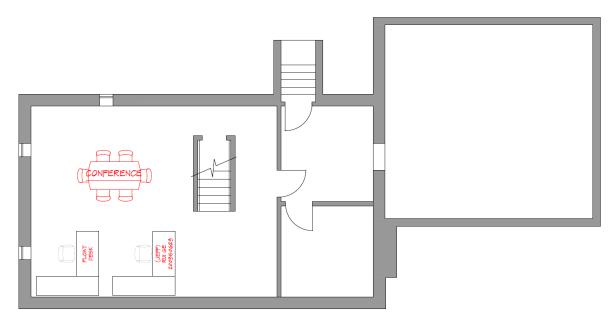







LEARNING ACCESS PROGRAM

E-Wing - Main Level 100

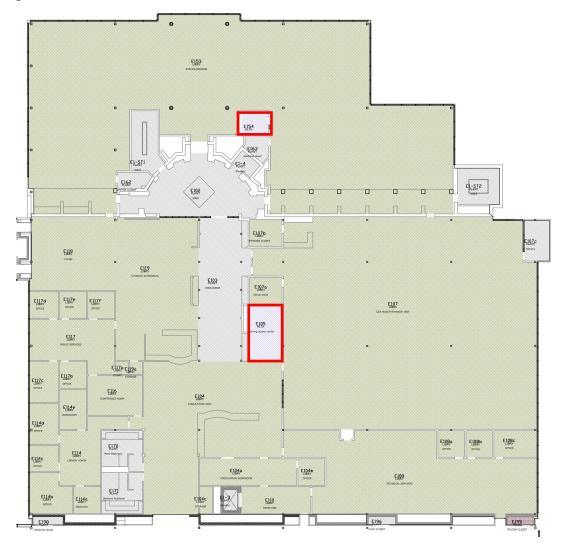




Dept Code	Dept Name	Area
HLTH	Health & Wellness	294
LIBRY	Library Services	24,920
PLANT	Plant Operations	2,892
TELEC	Telecommunications & Network Infrastructure	26
Total		28,132






LEARNING ACCESS PROGRAM


H-Wing - Main Level 100

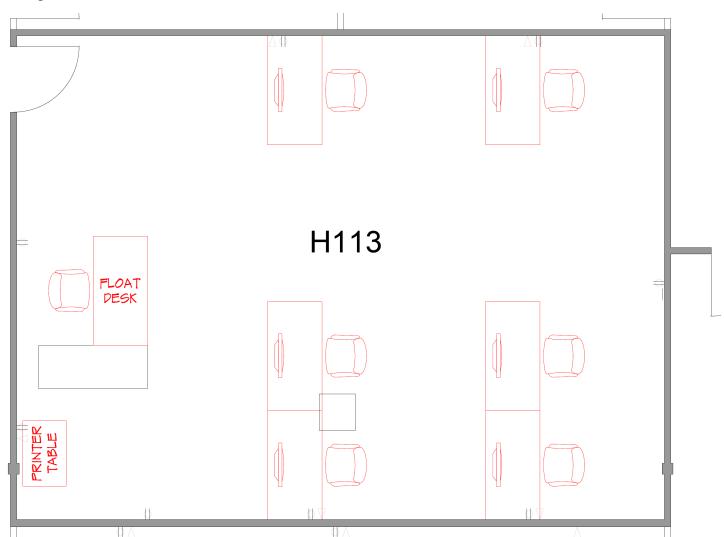




HRC & READING ROOM

E-Wing - Upper Level 200

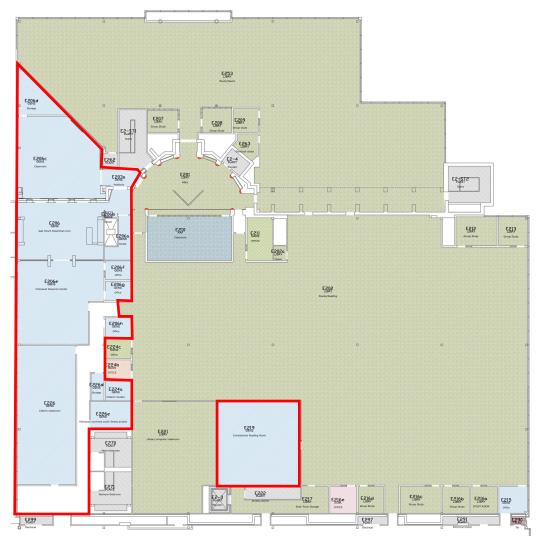





Dept Code	Dept Name	Area
AAF	Academic Affairs	473
BUSN	School of Business	64
GENS	School of General Studies	5,088
LIBRY	Library Services	20,112
NAMS	School of Natural Sciences and Math	201
PLANT	Plant Operations	1,065
SOBL	Social and Behavioral Sciences	90
TELEC	Telecommunications & Network Infrastructure	15
Total		27,108





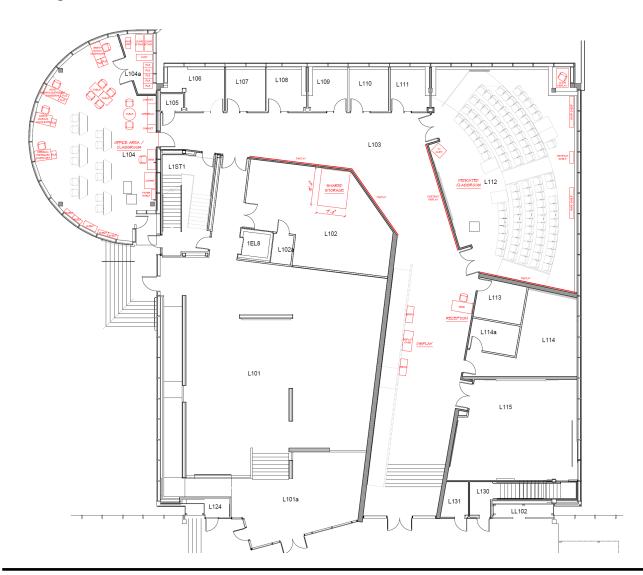






ARHU MEDIA PRODUCTION

E-Wing - Lower Level 000






Dept Code	Dept Name	Area
ADF	Adminstration and Finance	4,512
ARHU	School of Arts and Humanties	2,477
GRAPH	Graphics	2,264
LIBRY	Library Services	11,485
MEDIA	PRODUCTION SERVICES	4,256
PLANT	Plant Operations	1,403
TELEC	Telecommunications & Network Infrastructure	20
Total		26,417







ARHU MEDIA PRODUCTION

A-Wing - Lower Level 000 & Main Level 100 (Alton Auditorium)

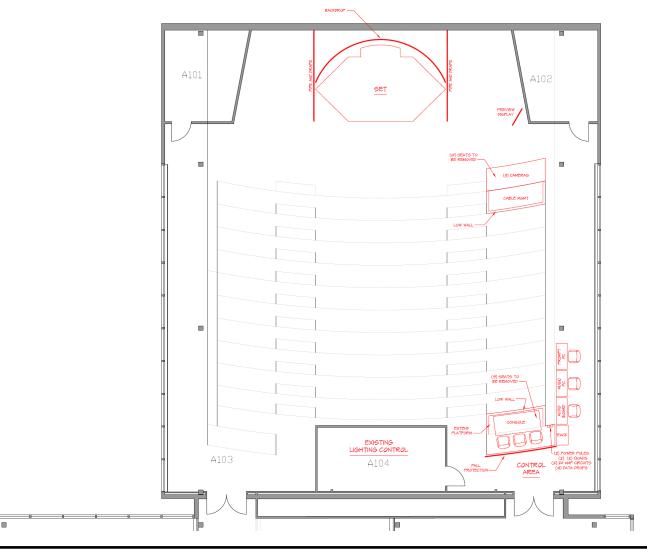



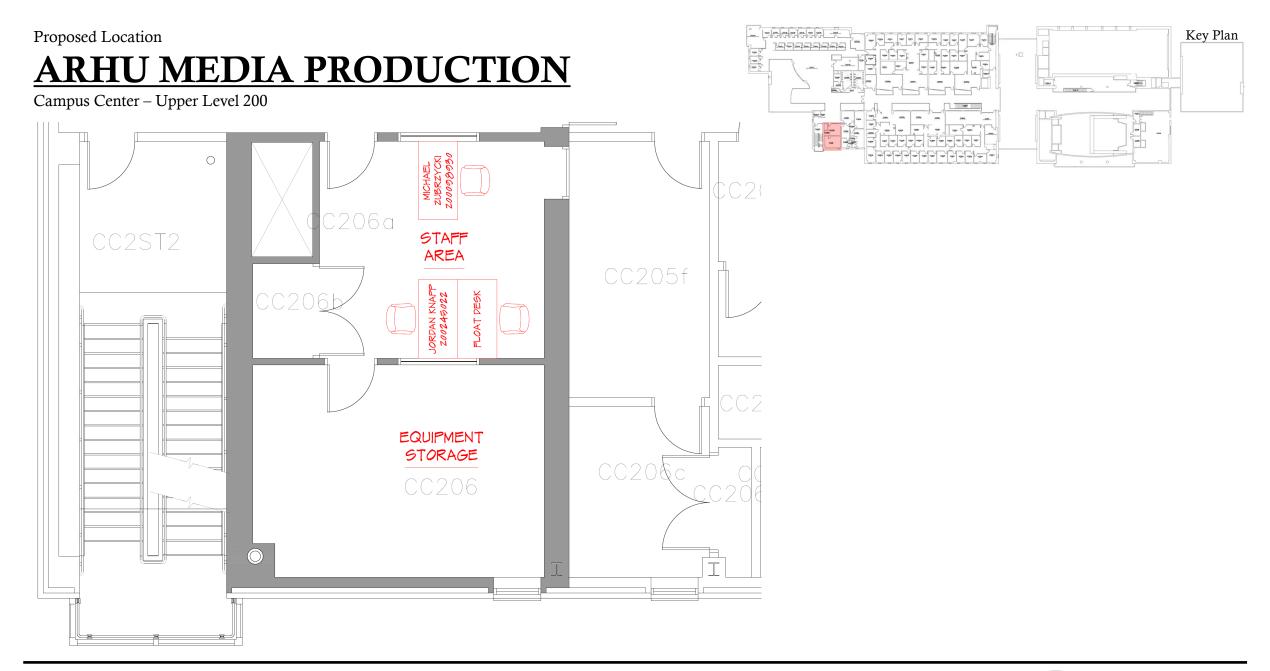






ARHU MEDIA PRODUCTION

Arts & Sciences Building – Main Level 100 & Upper Level 200

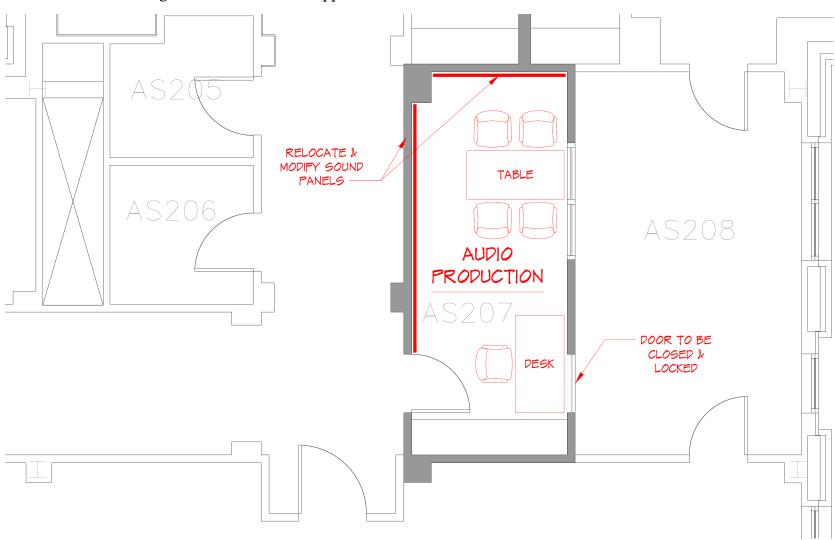









ARHU MEDIA PRODUCTION

G-Wing – Main Level 100

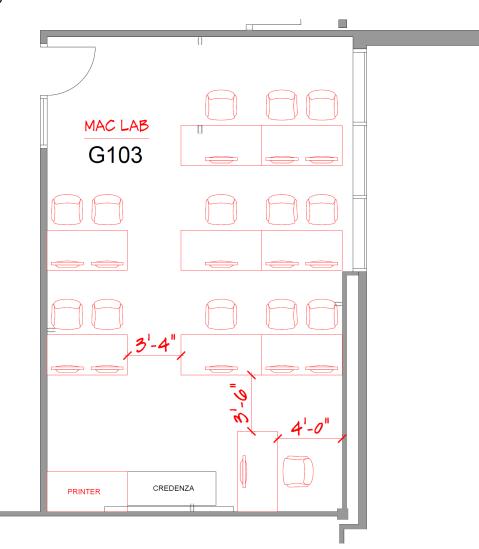



Overal1

PROJECT SCHEDULE

Today
12024 12025 12026

Start Sun 10/1/23 Finish Tue 9/1/26

Design / Relocation / Construction

ask Name	Duration	Start	Finish S	O N D J F M A	A M J A S O N D J F M A M J J A S O N D J F M A M J J A S O
ibrary Learning Commons	762 days	Sun 10/1/23	Tue 9/1/26		
Logistics Plan	164 days	Sun 10/1/23	Wed 5/15/24		Logistics Plan
Rough Schematics	22 days	Wed 11/1/23	Thu 11/30/23	Rough Schematics	
Final Schematics	10 days	Fri 12/1/23	Thu 12/14/23	Final Schematics	
Design Development	92 days	Fri 12/15/23	Mon 4/22/24		Design Developmen
Move Out	79 days	Wed 5/15/24	Sun 9/1/24		Move Out
Construction Drawings	95 days	Tue 4/23/24	Sun 9/1/24		Construction Drawings
State Comptroller Submission / Review	22 days	Mon 9/2/24	Tue 10/1/24		State Comptroller Submission / Review
Out to Bid	23 days	Wed 10/2/24	Fri 11/1/24		Out to Bid
Bid Review / Award / Contract	43 days	Mon 11/4/24	Wed 1/1/25		Bid Review / Award / Contract
Construction	368 days	Thu 1/2/25	Mon 6/1/26		Construction
Move in	66 days	Tue 6/2/26	Tue 9/1/26		Move i
				WE ARE HERE	
Logistics Phase				HERE	CONSTRUCTION LABOR DAY
Design Phase				LO	OGISTICS ² STARTS 2026
Relocation Phase State Review Phas				_	MOVES
Bidding / Contrac					LOGISTICS'
Construction Phase				SCHEDULE DETAIL	





Logistics

DETAILED LOGISTICS SCHEDULE

Today

| Half 1, 2024 | Half 2, 2024 |
| Start | Finish | Mon 9/2/24 |

Relocation / Swing Space Activation

ask Name	Duration	Start	Finish	September 2023 October 2023 November 2023 December 2023 January	2024 February 2024 March 2024 April 2024	May 2024 June 2024 July 2024 August 2024 September 2024 October 2024
ibrary Learning Commons - Logistics	235 days	Sun 10/1/23	Fri 8/23/24			Library Learning Commons - Logi
Logistics Plan	120 days	Sun 10/1/23	Fri 3/15/24		Logistics Plan	
Meet w/ Stakeholders	45 days	Sun 10/1/23	Thu 11/30/23	Meet w/ Stakeholde	ers	
Develop Logistics Plan	26 days	Fri 12/1/23	Fri 1/5/24	, D	evelop Logistics Plan	
Develop Improvement Plan	50 days	Mon 1/8/24	Fri 3/15/24	*	Develop Improv	ement Plan
Relocation	165 days	Mon 1/8/24	Fri 8/23/24			Relocation
ARHU	65 days	Mon 5/13/24	Fri 8/9/24			ARHU
Clear Alton / CC206 / AS207 / G103	5 days	Mon 5/13/24	Fri 5/17/24			Clear Alton / CC206 / AS207 / G103
Alton Reno	5 days	Mon 7/8/24	Fri 7/12/24			Alton Reno
Alton Data	5 days	Mon 7/15/24	Fri 7/19/24			Alton Data
Alton Relocation (Lerro)	10 days	Mon 7/29/24	Fri 8/9/24			Alton Relocation (Lerro)
G103 Move	5 days	Mon 7/8/24	Fri 7/12/24			G103 Move
AS207 Move	5 days	Mon 7/22/24	Fri 7/26/24			AS207 Move
CC206 Move	5 days	Mon 8/5/24	Fri 8/9/24			CC206 Meve
Library Services	140 days	Mon 2/5/24	Fri 8/16/24		C/D Atrium Electric	Library Services
C/D Atrium Electric	5 days	Mon 2/5/24	Fri 2/9/24			
H114 Data	5 days	Mon 3/11/24	Fri 3/15/24		★ H114 Data	
C012 Data	5 days	Mon 3/11/24	Fri 3/15/24		C012 Data	
Pomona Data	5 days	Mon 3/11/24	Fri 3/15/24		Pomona Data	
C/D Atrium Data	5 days	Mon 3/11/24	Fri 3/15/24		★ C/D Atrium Data	
Clear C001 / C002 / C012 / H114	5 days	Mon 5/13/24	Fri 5/17/24	LIBRARY SERVICES		Clear C001 / C002 / C012 / H114
C001 Demo	5 days	Mon 5/13/24	Fri 5/17/24	LIDKAKI SEKTICES		C001 Demo
Library Collections Staging (LMR)	3 days	Wed 5/15/24	Fri 5/17/24	& MOVING SERVICES		Library Collections Staging (LMR)
Library Collections Packing (LMR)	10 days	Mon 5/20/24	Fri 5/31/24	& MOVING SERVICES		Library Collections Packing (LMR)
Library Collections Relocation (LMR)	5 days	Mon 6/3/24	Fri 6/7/24			Library Collections Relocation (LMR)
H114 Move	5 days	Mon 5/20/24	Fri 5/24/24			H114 Move
C001 / C002 Stack Relocation	5 days	Mon 5/27/24	Fri 5/31/24			C001 / C002 Stack Relocation
C012 Move	5 days	Mon 6/10/24	Fri 6/14/24			C012 Move
Pomona House Move	5 days	Mon 6/24/24	Fri 6/28/24			Pomona House Move
C/D Atrium Move	10 days	Mon 8/5/24	Fri 8/16/24			C/D Atrium Move
Follet	110 days	Mon 1/8/24	Fri 6/7/24			Follet
Clear F003	18 days	Mon 1/8/24	Wed 1/31/24	<u>-</u>	Clear F003	•
Demo F003	5 days	Mon 3/11/24	Fri 3/15/24		Demo F003	
Demo F020	5 days	Mon 3/11/24	Fri 3/15/24	BOOK DEPOT	Demo F020	
F003 Data (ITS)	5 days	Mon 4/22/24	Fri 4/26/24		-	F003 Data (ITS)
F003 Reno	55 days	Mon 3/18/24	Fri 5/31/24	(CURRENTLY UNDERWAY)		F003 Reno
F003 Data (Follett)	5 days	Mon 6/3/24	Fri 6/7/24	(COMMENTED CIVIDER (VIII)	•	F003 Data (Follett)
Follett Move	5 days	Mon 6/3/24	Fri 6/7/24			Follett Move
Graphics	80 days	Mon 4/15/24	Fri 8/2/24		-	₩ URM Data (F001)
URM Data (F001)	5 days	Mon 4/22/24	Fri 4/26/24			
Sprinkler Head Relocation (TDK)	5 days	Mon 4/15/24	Fri 4/19/24			Sprinkler Head Relocation (TDK)
Install URM Storefront (SJG)	5 days	Mon 4/22/24	Fri 4/26/24		•	Enstall URM Storefront (SJG) F001 (URM) Move
F001 (URM) Move	5 days	Mon 7/29/24	Fri 8/2/24			FUU I (UKIVI) IVIOVE
Production Services	100 days	Mon 4/8/24	Fri 8/23/24			Production Services
F004 Data	5 days	Mon 4/22/24	Fri 4/26/24	PRODUCTION SERVICES		<u>v </u>
Relocate Rowing	5 days	Mon 4/8/24	Fri 4/12/24		≠ Re	elocate Rowing
F004 Reno	90 days	Mon 4/15/24	Fri 8/16/24	(CURRENTLY UNDERWAY)		F004 Feno
F004 Move	5 days	Mon 8/19/24	Fri 8/23/24	(CORRENTLI UNDERWAI)		F004 Move
Learning Access Program	55 days	Mon 3/11/24	Fri 5/24/24			Learning Access Program
H113 Data	5 days	Mon 3/11/24	Fri 3/15/24		★ H113 Data	
Clear H113	5 days	Mon 5/13/24	Fri 5/17/24			Clear H113
	5 days	Mon 5/20/24	Fri 5/24/24			H113 Move
H113 Move		Mon 3/11/24	Fri 7/5/24			Holocaust Resource Center
H113 Move	95 days		111//3/24		★ L104 Data	•
H113 Move Holocaust Resource Center	85 days					
H113 Move Holocaust Resource Center L104 Data	5 days	Mon 3/11/24	Fri 3/15/24		*	— Clear I 104
H113 Move Holocaust Resource Center L104 Data Clear L104	5 days 5 days	Mon 3/11/24 Mon 5/13/24	Fri 3/15/24 Fri 5/17/24		2.5.5	Clear L104
H113 Move Holocaust Resource Center L104 Data	5 days	Mon 3/11/24	Fri 3/15/24			Clear L104 L104 / L112 Move
H113 Move Holocaust Resource Center L104 Data Clear L104	5 days 5 days 5 days	Mon 3/11/24 Mon 5/13/24 Mon 7/1/24	Fri 3/15/24 Fri 5/17/24 Fri 7/5/24		*	<u> </u>
H113 Move Holocaust Resource Center L104 Data Clear L104 L104 / L112 Move	5 days 5 days	Mon 3/11/24 Mon 5/13/24	Fri 3/15/24 Fri 5/17/24		*	L104 / L112 Move





Logistics

DETAILED LOGISTICS SPREADSHEET

Relocation / ITS / Access Control

						PLANT MANAGEMENT			ITS		ACCESS CONTROL				
Room #	Room Name	Department	Space Type	Max Occupant Load	# of Permanent Occupants	Permanent Occupant Name	Z#	Work Remote Yes / No Hybrid	Temporary \ Swing Location	# Of Boxes To Be Moved	Special Items To Be Moved	New Activation (Y/N)	Old Deactivation (Y/N)	New Activation (Y/N)2	Old Deactivation (Y/N)2
E001a	Office	Bookstore	Office (310)	1	1	Affiliate		No	F003	2					
E001b	Office	Bookstore	Office (310)	1	1	Affiliate		No	F003	2					
E014	General Office	Graphics	Office (310)	6	3	Alten, Margot	Z00157778	Yes	F001 (Production Space)	0					
E006a E108	Office Technical Services Suite	Production Services Library Services	Office (310)	1	1	Aungst, Shannon Barnabei, Nicole	Z00016707 Z00088543	No No	F004 C012	0					
E108 E021d		Production Services	Central Comp or Telecomm (710) Office (310)	1	1	Beck, John	Z00088543 Z00007664	No	F004	0					
E006		Production Services	Office (310)	-		Berardo, Nikola	Z00312289	No	F004	0					
E021	Technical Operations	Production Services	Central Comp or Telecomm (710)	0		Bove, Dino	Z00013323	No	F004	0					
E021e	Office	Production Services	Office (310)	1		Brandhorst, Robert	Z00012501	No	F004	0					
E012	General Office	Graphics	Office (310)	3	2	Brignola, Jena	Z00010266	Yes	F001 (Production Space)	0					
E108		Library Services	Central Comp or Telecomm (710)	-		Bucikowski, Susan	Z00015195	No	C/D Atrium	4					
E021a		Production Services	Office (310)	1	1	Chew, Scott	Z00177567	No	F004	0					
E224c	Office	School of Natural Sciences and Math	Office (310)	2	2	Colby, Richard	Z00009099	ļ.,	NAMS Adjunct Office						
E108		Library Services	Central Comp or Telecomm (710)	-	-	Comer, Charla	Z00012121 Z00426294	No.	C/D Atrium	4					
E006 E013	General Office Photo Studio	Production Services Graphics	Office (310) Office (310)	2	1	De Pompo, Matthew DeLury, Bernard	Z00426294 Z00199708	No Yes	F004 F001 (Production Space)	0					
E104	Circulation Desks	Library Services	Office (310)	5	5	Demosthenes, Shekhania	Z00199708 Z00114879	No.	C/D Atrium	20					
		Library Services	Office (310)	1	1	Destasio, Joyce	700384755	No	H114	5					
E104		Library Services	Office Service (315)	-	-	Devonshire, Taylor	Z00399922	No	Pomona House	3					
E108	Technical Services Suite	Library Services	Central Comp or Telecomm (710)	-	-	Disciascio, Lisa	Z00151035	No	C/D Atrium	4					
E216e	Office	School of Social and Behavioral Sciences	Office (310)	2	1	Ferri, Christine	Z00081912		F231						
E114		Library Services	Office (310)	0	1	Gazsi, Patricia	Z00012779	No	C012	3					
E117c		Library Services	Office (310)	1	1	Ge, Rui (Jeff)	Z00350623	No	Pomona House	2					
E006	General Office	Production Services	011100 (020)	12	9	Georgel, Nicholas	Z00272749	No	F004	0					
E104	Circulation Desks	Library Services	Office Service (315)	-	-	Gipson, Tiffiny	Z00212841	No	C/D Atrium	20					
E211 E006	Office General Office	School of Arts and Humanities Production Services	Office (310)	3	2	Grasso, Norma Green, Kent	Z00013822 Z00148692	No	Passed Away F004	0					
E224b	Office	School of Business	Office (310) Office (310)	1	1	Han, Jung An	Z00342670	INO	Retiring	U					
E014	General Office	Graphics	Office (310)			Hartley, Heidi	Z00162220	Yes	F001 (Production Space)	0					
E104	Circulation Desks	Library Services	Office Service (315)	-	-	Jackson, Dana	Z00167416	No	C/D Atrium	3					
E005		Production Services	Office (310)	1	1	Jackson, Mark	Z00001438	No	F004	85					
E107	Commons Info Desk	Library Services	Stack (420)	1	2	Jacuk, Patrice	Z00277301	No	C/D Atrium	2					
E117e	Office	Library Services	Office (310)	1	1	Jeitner, Eric	Z00249016	No	H114	3					
E006	General Office	Production Services	Office (310)	-	-	Kenzien, Emilee	Z00423639	No	F004	0					
E041	Office	School of Arts and Humanities	Office (310)	1	1	Knapp, Jordan	Z00245022	No	CC206	5					
E108b	Office	Library Services	Office (310)	1	1	Lombardo, Jaime	Z00104018	No	Pomona House	4					
E114c E206h	Office Office	Library Services School of General Studies	Office (310)	1	1	Lutgen, Karen Marcus, Steven	Z00217024 Z00062635	No	Pomona House L104	3					
E206h E006	General Office	Production Services	Office (310)	1	1	Martinez, Amanda	Z00062635 Z00207193	No	F004	0					
E117d	Office	Library Services	Office (310)	1		Martotano, Jessica	Z00207193 Z00293476	No	H114	5					
E1170 E104	Circulation Desks	Library Services	Office (S10)	-	-	Mettrock, Donna	Z00293476 Z00183344	No	C/D Atrium	5					
E206f	Office	School of General Studies	Office (310)	1	1	Moreno-Rodriguez, Irvin	Z00192904	No	L104	75					
E006	General Office	Production Services	Office (310)	-	-	Mortillite, Perry	Z00215272	No	F004	0					
E006	General Office	Production Services	Office (310)	-	-	Pavia, Cheryl	Z00020449	No	F004	0					
E055	Office	Library Services	Office (310)	1	1	Perez, Heather	Z00316433	No	C012	6					
E014b		Graphics	Office (310)	1	1	Quinn, Karen	Z00017560	Yes	F001 (Production Space)	0					
E117b		Library Services	Office (310)	1		Riehl, Cheyenne	Z00420739	No	H114	4					
E206 E206	Gail Hirsch Rosenthal Room Gail Hirsch Rosenthal Room	School of General Studies School of General Studies	Exhibit Space (625)	2	2	Roach, Brett	Z00250659 Z00196787	No No	L104 L104	0					
E043b		Production Services	Exhibit Space (625) Media Production Service (535)	0	1	Rodriguez, Rebecca Ryan, William	Z00196787 Z00105903	No No	F004	0					
E0438		Graphics	Office (310)	-	-	Schenck, Gary	Z00103903 Z00011813	Yes	F001 (Production Space)	0					
E012		Graphics	Office (310)	-	-	Schocklin, Ryan	Z00011013	Yes	F001 (Production Space)	0					
E114d		Library Services	Office (310)	1	1	Stamatopoulos, Konstantinos	Z00187200	No	Pomona House	3					
E224c	Office	School of Natural Sciences and Math	Office (310)	-	-	Stiles, Lynn	Z00014206		No Longer on Campus						
E108		Library Services	Central Comp or Telecomm (710)	-	-	Sussmeier, Stephanie	Z00139889	No	Pomona House	10					
E114b		Library Services	Office (310)	1	1	Thatcher, Patricia	Z00400710	No	Pomona House	3					
E056		Library Services	Office Service (315)	1	1	Tillstrom, Louise	Z00014169	No	C012	6					
E006	General Office	Production Services	Office (310)	-		Topping, Jeffrey	Z00249258	No	F004	U					
E215 E108c	Office Office	School of General Studies Library Services	Office (310)	4	1	Van Duyne, Emily	Z00106678 Z00266275	No	F235 Pomona House	0					
E012a	Office	Graphics	Office (310) Office (310)	1		Wadley, Natalie Wuillermin, Edward	Z00266275 Z00361443	Yes	F001 (Production Space)	55					
E211	Office	School of Natural Sciences and Math	Office (310)	-		Zimmerman, George	Z00003098	163	No Longer on Campus	33					
F031		School of Arts and Humanities	Office (310)	1		Zubrzycki, Michael	Z00098930	No	CC206	50					
2001		or Ar & and maintainines	011102 (010)	•	-	your, morraei	_00058550	1	1	1					







LIBRARY LEARNING COMMONS

Plans for Renovation to the Academic Spine, E - Wing
